



New DPW Facility Construction Update

October 15, 2024

New DPW Facility Overall Schedule

- VJS (construction company) mobilize on-site June 2024.
- CW Purpero (environmental remediation contractor) mobilize on-site July 2024.
- Building 1 (main building) complete July 2025.
- Building 2 (secondary building) complete late July 2025.
- Building 5 (cold storage) complete early August 2025.
- Building 4 (fuel island) complete May 2025
- Project Completion - September 2025



Major Items Completed to Date

- Scraping of topsoil and clay cap.
- Excavation and filling of the “hot spots”.
- Site grading.
- Submittal of environmental documents to DNR for transfer station site.
- Submittals for electric and gas service to site.

Site in
August




Site in
October



Current Items Being Worked On

- **Rammed Aggregate Piers** - This process is different than typical piers. There is no pounding. The rig pushes (rams) the soil deeper into the ground and then gravel is poured into the hole and building.

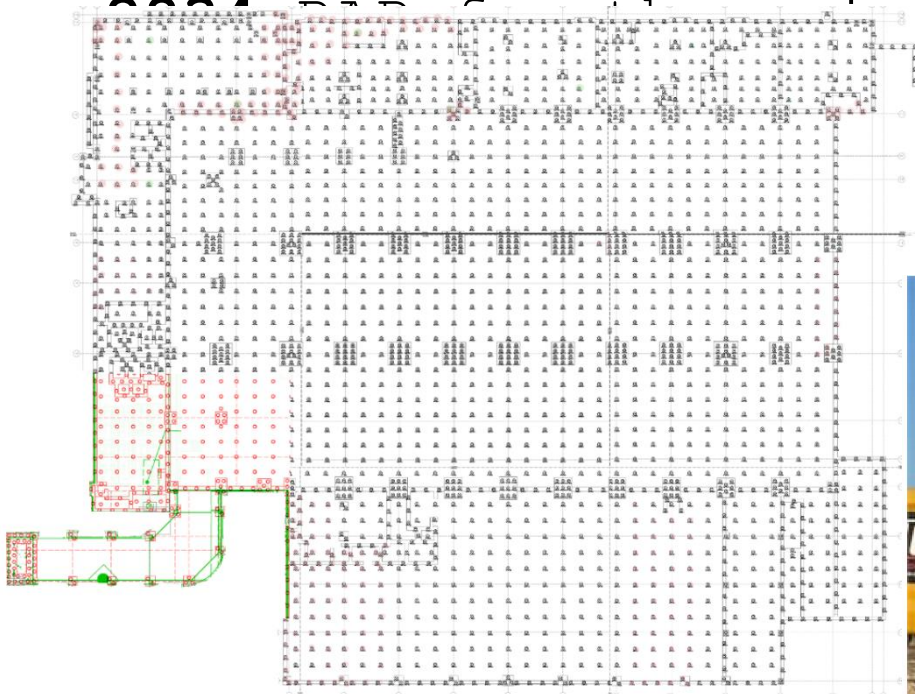

Current Items Being Worked On

- **Footings and Foundations** – These are the start of the walls around the building

Looking east along W. Burnham St.



Looking at front doors!



Looking north along S. 53rd St.

Site Pictures from VJS



Site Pictures from VJS



Site Pictures from VJS



Site Pictures from VJS



Site Pictures from VJS



Thank you!

